Lecture 4

IT Project Scope Management

Project scope management is defining and controlling what is or is not included in a project

During Planning

1- Planning Scope (Define scope management)

- determining how the project's scope and requirements will be managed
- E.g., Using product backlog or requirements statement at start?

2- Collecting requirements

- use an **iterative approach** to defining requirements since they are often unclear early in a project
- **Methods** includes -- Interviewing, Focus groups, group and decision-making techniques, Questionnaires and surveys, Observation, Prototyping, **benchmarking** (comparing with other projects)
- **Requirements traceability matrix (RTM)** -> is a table that lists requirements, various attributes of each requirement, and the status of the requirements to ensure that all requirements are addressed

Requirement No.	Name	Category	Source	Status
R32	Laptop memory	Hardware	Project charter and corporate laptop specifications	Complete. Laptops ordered meet requirement by having 4GB of memory.

3-Define scope

- Creating a **scope statement**
- Scope statements
  1) **must include:** scope description, project deliverables, acceptance criteria
  2) **can include:** project boundaries, constraints, and assumptions.

Project Scope Statement Example			
Project Name	IVR Project		
Project Sponsor	Dave Sponsor	Project Manager	Alice Michaels
Date of Project Approval	08 March 2015	Last Revision Date	08 March 2015
Scope Description	IN SCOPE: - An IVR system to handle and direct sales calls. - Setup of the IVR system ready to handle all sales enquiries - Training for the sales team on how to use the system - An administration system so the IVR system can be configured by the sales team OUT OF SCOPE: - Support for any other team other than sales - The ability to route complex sales enquiries, such as partnerships etc.		
Project Deliverables	- A customer facing IVR system - An IVR configuration system - A training manual for new and existing sales team members		
Acceptance Criteria	The project will be accepted when it is agreed by the sale team that the deliverables meet their needs (deliverables signed off). The project will also be considered a success if post launch testing shows that customer satisfaction is over 5 points higher than where it is now.		
Constraints	The sales team are not dedicated to this project, and must fit this around their day-to-day sales jobs.		
Assumptions	A sales team & full project team will be available to co-create the WBS		

4-Creating Work Breakdown Structure (WBS)

- **subdividing the deliverables** into smaller components (decomposition)
- **Approaches to develop a WBS**
  1) **Using guidelines**: Some organizations, provide guidelines for preparing WBSs

2) **Analogy approach:** Review WBSs of similar projects and tailor to your project
3) **Top-down approach:** Start with the largest items of the project and break them down
4) **Bottom-up approach:** Start with the specific tasks and roll them up
5) **Mind-mapping approach**: uses branches radiating out from a core idea to structure thoughts and ideas

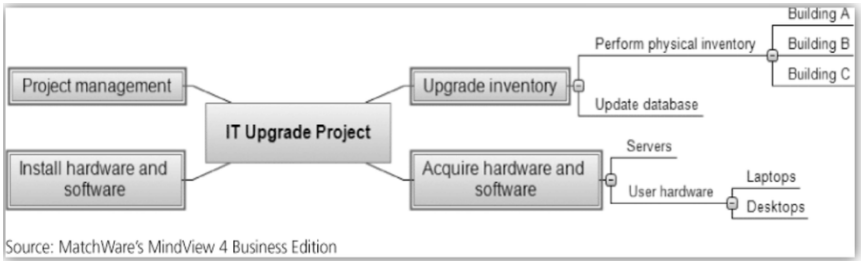

- A **WBS dictionary** is a **document** that **describes detailed information about each WBS item**
- A **work package** is a task at the abstract level of the WBS
- The **scope baseline** includes
    1) approved project scope statement
    2) its associated WBS and
    3) WBS dictionary

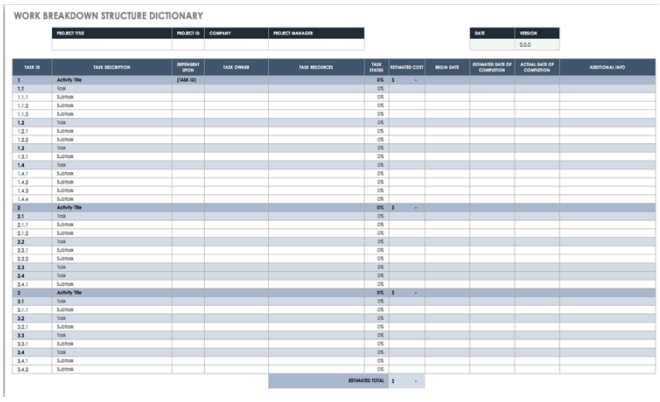

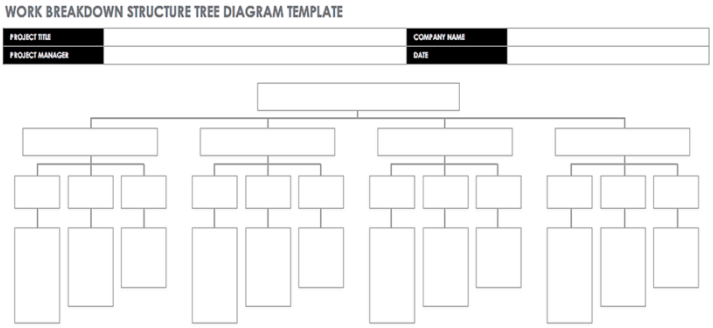

During Monitoring & Controlling

5-Validating scope

- **formal acceptance** of the project deliverables (achieved by a **customer inspection**)

6- Controlling Scope

- controlling changes to project scope throughout the life of the project
